




Orange County Public Schools
 445 West Amelia St
 Orlando, FL 32801

Monthly Status Report—Updated 05/14/07
Comprehensive
West Orange HS Replacement



Area Supt.	Dr. Rosita Riley
Principal	Dr. Daniel Buckman
Student Stations	2922 S. S. 2776 Capacity
Architect	Schenkel Shultz
Contractor	Clark Construction

SCOPE

Construction of a replacement Prototype High School on the existing school site.


Construction Schedule: **Start: Oct 24, 2006** **Scheduled Completion: Apr 17, 2009**

Project Summary:
 Construction is 18% complete.

Project Budget Information:

Project Budget	\$85,000,000
	\$ 0.00
Current Budget	\$85,000,000

Directions to site

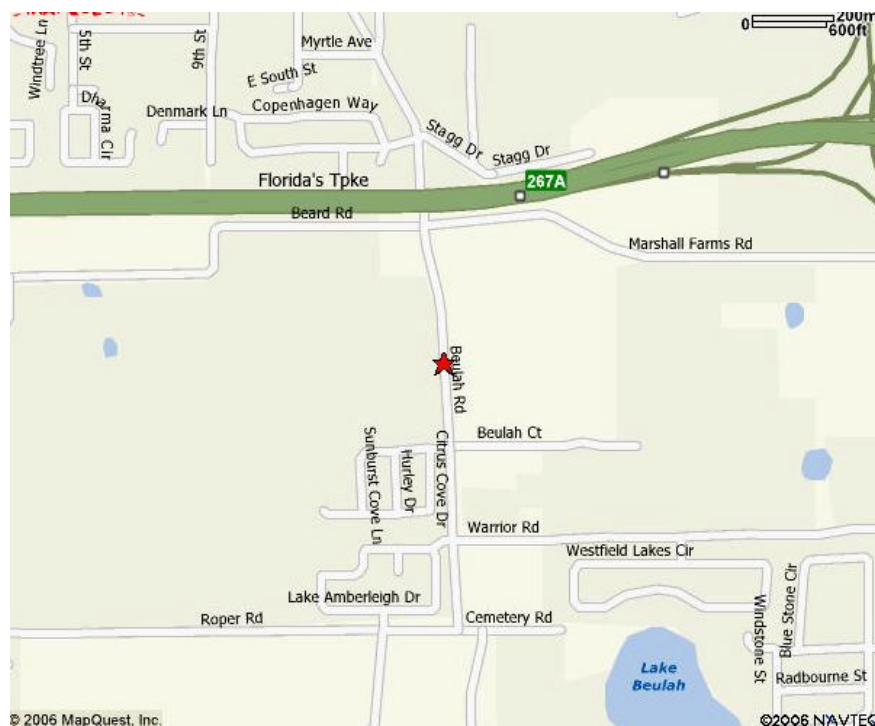

From the intersection of Colonial Dr. and Orange Ave., proceed west on Colonial Dr. approximately 15 miles to Beulah Rd., turn left. Proceed south on Beulah Rd. under the Sunshine State Pkwy. Proceed approximately 1/4 mile and the school is located on the left side of Beulah Rd.
